

MAR 23

PLUMBING INSPECTION REPORT

M


My Site

TUESDAY 21st April 2026

91.3 %

(21.0/23.0)

SCORE BY SECTION

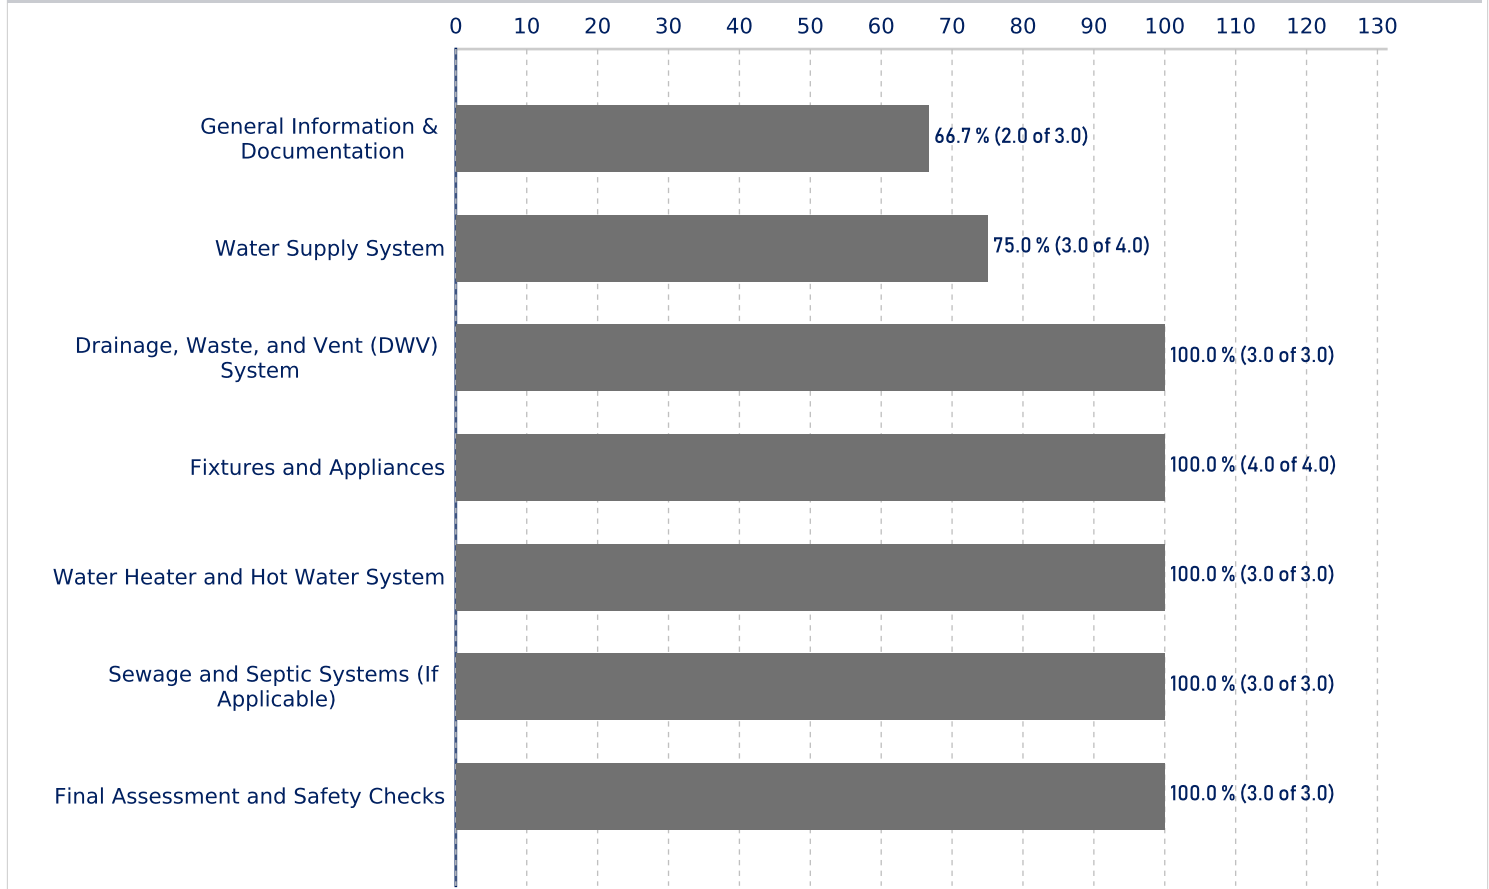

Section	Actual	Target	%	Section	Actual	Target	%
General Information & Documentation	2.0	3.0	66.7	Water Supply System	3.0	4.0	75.0
Drainage, Waste, and Vent (DWV) System	3.0	3.0	100.0	Fixtures and Appliances	4.0	4.0	100.0
Water Heater and Hot Water System	3.0	3.0	100.0	Sewage and Septic Systems (If	3.0	3.0	100.0
Final Assessment and Safety Checks	3.0	3.0	100.0				

PLUMBING INSPECTION REPORT

GENERAL INFORMATION & DOCUMENTATION

(2/3) 66.7 %

Q#	QUESTION	SCORE	RESPONSE	PREVIOUS
1	Has the plumbing system been installed according to approved plans and building codes?	(1/1)	YES	
2	Are all necessary permits and inspection documents available and up to date?	(1/1)	YES	
3	Is the licensed plumber's information and certification included in the report?		N/A	
4	Have any previous plumbing issues or repairs been documented prior to inspection?	(0/1)	NO	

WATER SUPPLY SYSTEM

(3/4) 75.0 %

Q#	QUESTION	SCORE	RESPONSE	PREVIOUS
5	Are all water supply lines properly connected, labeled, and leak-free?	(1/1)	YES	
6	Is water pressure within the acceptable range (typically 40–80 psi)?		N/A	
7	Are shut-off valves present, accessible, and operational at all key fixture points?	(1/1)	YES	
8	Is the main water supply valve working and easily reachable in case of emergency?	(1/1)	YES	
9	Are backflow prevention devices installed and functioning where required?	(0/1)	NO	

DRAINAGE, WASTE, AND VENT (DWV) SYSTEM

(3/3) 100.0 %

Q#	QUESTION	SCORE	RESPONSE	PREVIOUS
10	Are all drains clear, with proper slope and venting to prevent backups or odor?	(1/1)	YES	
11	Are traps installed under sinks, tubs, and floor drains as required?		N/A	
12	Are vent stacks unobstructed and extended above the roofline?	(1/1)	YES	
13	Is the DWV system free from leaks, corrosion, or loose fittings?	(1/1)	YES	
14	Has a water or smoke test been conducted to check for hidden leaks in the drainage system?		N/A	

FIXTURES AND APPLIANCES

(4/4) 100.0 %

Q#	QUESTION	SCORE	RESPONSE	PREVIOUS
15	Are all plumbing fixtures such as sinks, toilets, bathtubs, and showers securely mounted and operating correctly?	(1/1)	YES	
16	Is hot water reaching fixtures within a reasonable time from activation?	(1/1)	YES	
17	Are toilets flushing properly and not running continuously?	(1/1)	YES	
18	Are faucets and valves operating smoothly with no drips or signs of wear?	(1/1)	YES	
19	Are dishwashers, washing machines, and water heaters properly connected and vented?		N/A	

PLUMBING INSPECTION REPORT

WATER HEATER AND HOT WATER SYSTEM (3/3) 100.0 %

Table with 5 columns: Q#, QUESTION, SCORE, RESPONSE, PREVIOUS. Contains 5 rows of inspection questions regarding water heater installation and safety.

SEWAGE AND SEPTIC SYSTEMS (IF APPLICABLE) (3/3) 100.0 %

Table with 5 columns: Q#, QUESTION, SCORE, RESPONSE, PREVIOUS. Contains 4 rows of inspection questions regarding sewage and septic systems.

FINAL ASSESSMENT AND SAFETY CHECKS (3/3) 100.0 %

Table with 5 columns: Q#, QUESTION, SCORE, RESPONSE, PREVIOUS. Contains 5 rows of final assessment and safety check questions.

DECLARATION

Handwritten signature of the auditor.

Auditor (Aashiqe Rasul)
